| Task Name |
|---|
| Initial Study |
| **Task 1 - Technical Steering Committee Meeting** |
| **Task 2 - Development of Geodatabase** |
| 2.1 Develop the Geodatabase |
| 2.2 Incorporate Project data |
| **Task 3 - Aquifer Recharge Assessment** |
| 3.1 Infiltration Testing |
| **3.2 Stream Gauging** |
| Gauge Installation |
| **Stream Gauge Monitoring 2010** |
| **Stream Gauge Monitoring 2011** |
| **Stream Gauge Monitoring 2012** |
| **3.3 Stream-Aquifer Temperature Gradient** |
| Probe Installation |
| **Temperature Profile Monitoring** |
| Seepage Meter Observations |
| Slug Testing |
| Task 4 - Installation of Groundwater Monitoring Wells |
| Task 5 - Aquifer Performance Testing |
| Task 6 - Public Outreach, Education, and Coordination |
| **Reporting** |
| Monthly Status Reports |
| **Quarterly Reports** |
| **Technical Reports** |
| Field Investigation Report |
| Geodatabase Implementation Report |
| Aquifer Testing Report |
| Recharge Assessment Report |
| Final Comprehensive Report |

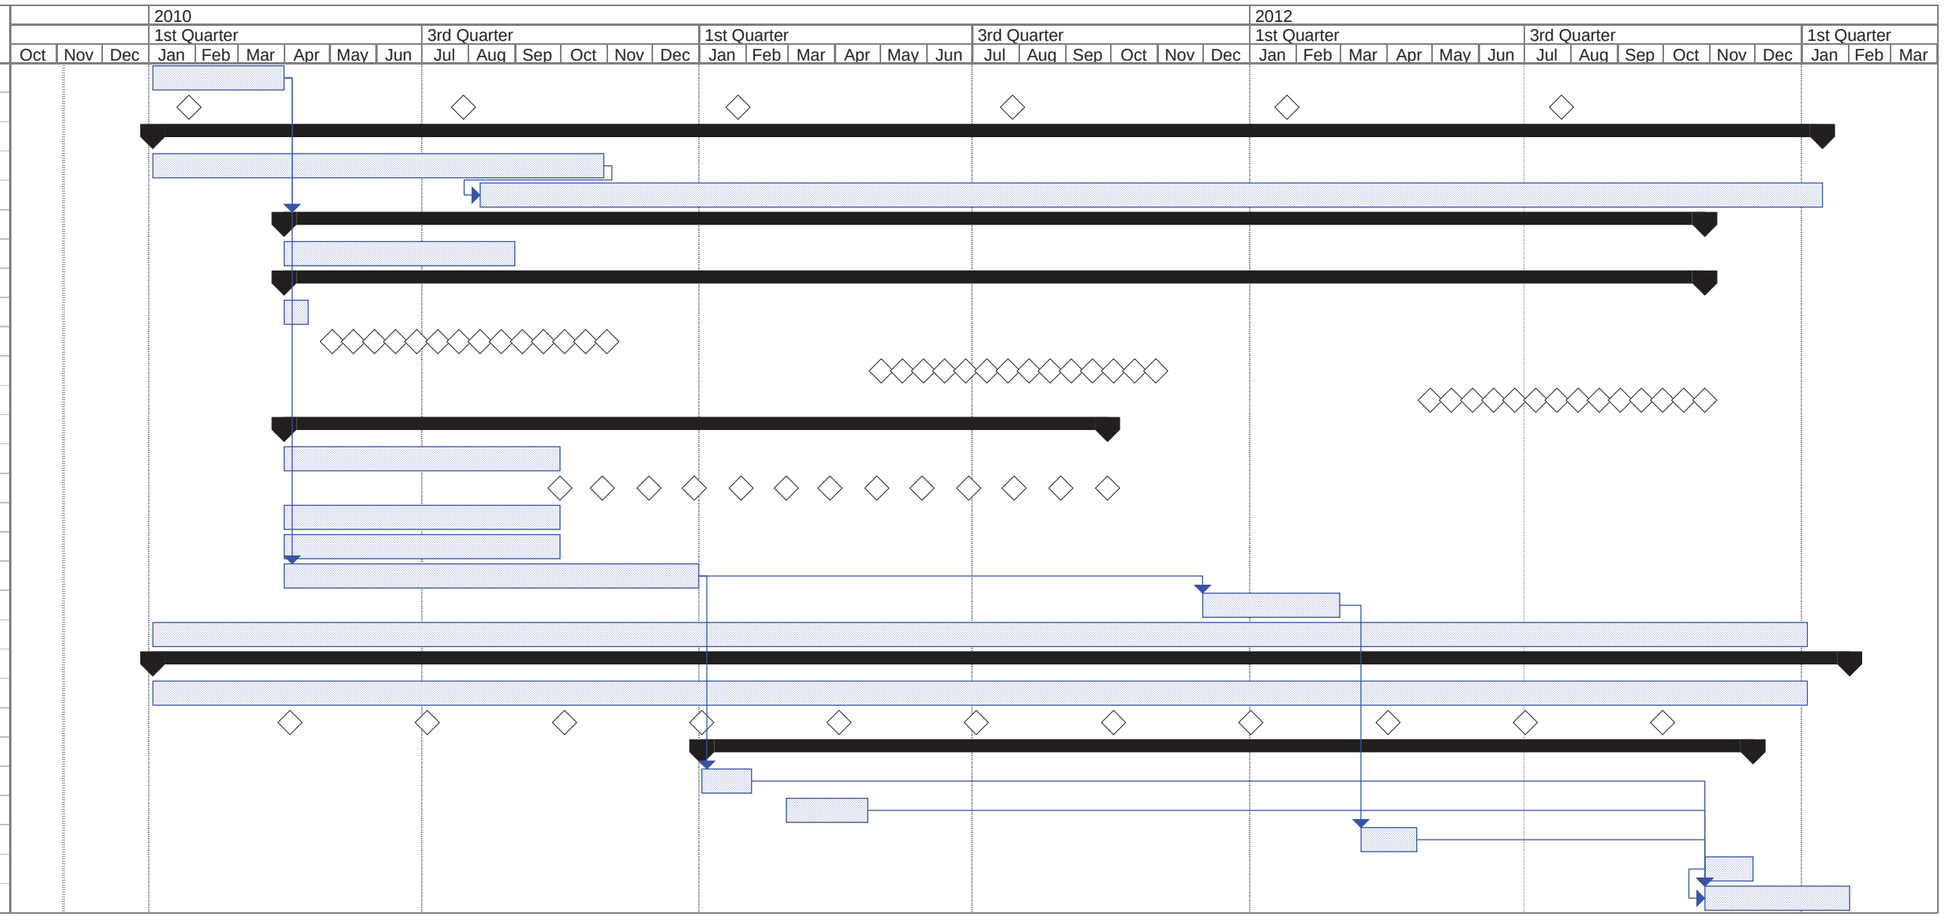


*Figure 5.2. BC's preliminary project schedule tracks significant deliverables, field-based efforts, and community outreach programs.*
